



Hired & Managed Advisory General Method Statement – Advanté Welfare

Scope

The scope of this General Method Statement is to provide an advisory document to confirm a sequenced statement of work for our arrival on site and delivery of an Advanté SOLAR EcoLogic 32 Ft x 9 Ft Welfare Unit in conjunction with client managed resources and site lifting plan requirements.

Our planning and controls have been developed in accordance with BS7121: 2016 Part 4 covering the provision of Hired & Managed Lifting operations in accordance with client Lifting Plans.

The sequencing outlined provides guidance on each step of this process from arrival on site, interaction with site resource, positioning of the vehicle for lifting and exiting the site post completion of the delivery.

In preparation for the new Civil Aviation Authority CAP 1096 Guidance Implementation which will occur not earlier than 1st April 2022, please notify Advanté Ltd if there are Aerodromes, Helipads or Private Landing Strips in the vicinity of the location of the enquiry and Advanté Ltd can advise on the notification process that the CAA will expect the Crane user to comply with based on the document link below.

<https://www.cpa.uk.net/news/caa-cap-1096-guidance-for-crane-users-and-associated-cpa-tin>

Collection of the SOLAR EcoLogic Unit will follow the same process. This may require interaction with Advanté in advance of the planned collection date with the site resource to highlight any differences in site conditions and access that have taken place after the original delivery.

We will ensure that all lifting information including records of competence and lifting equipment inspection and test are available for the client to review and assess on site.

Abbreviations used in this document.

LLCO – Lorry Loader Crane Operator

LLC – Lorry Loader Crane

C SM – Client Site Management referring directly to the receiver of this document


C Ops – Client Site Operatives organised by the C SM

RA – Risk Assessment

EL Unit – SOLAR EcoLogic Welfare Unit

1. Details of Load/confirmation of lifting radius allowed for/Corner loadings for intended position.

Weight (inc attachments):	SOLAR EcoLogic 1400 Unit or SOLAR EcoLogic 1700 Unit or SOLAR EcoLogic 1750 Unit or SOLAR EcoLogic 1850 Unit Maximum 7400 Kgs Each
Dimensions:	32 Ft x 9 Ft = L 9.75 M x W 2.74 M x H 2.50 M (
Height of Lift:	11.65 Metres to top of Jib minimum clearance needed
Max Radius:	7.95 Metres
Position of C of G:	Lower Lifting Lugs fabricated/positioned at the factory as per the Caption Photo below to suit the final C of G of the Unit - As per the manufacturer documentation

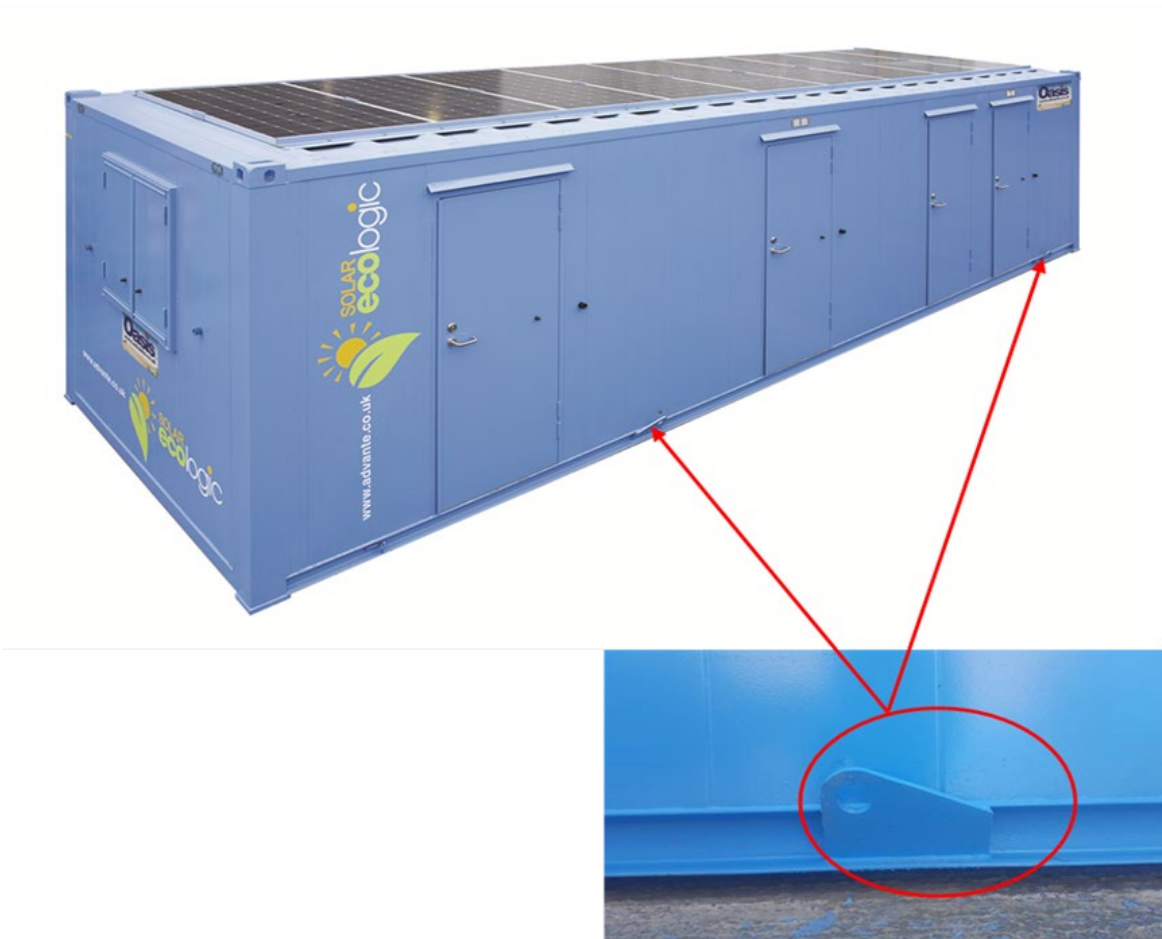



Version 1 1-3-2018

Loadings calculation for 9.75m (32ft) EcoLogic SOLAR Unit levelled on the Corner Post Steel Base 184 x 164 mm Plate


EcoLogic SOLAR Unit Max Weight 7400 Kgs - Max Weight when lifted from one end =	5052
Load per corner	2526
Total load per corner in Kg's	
Pad's NOT INCLUDED - Base Plate size under legs	184 by 164 mm

Pressure under each jackleg in N/m²	
2526	$M_L = \text{MASS OF TOTAL LOAD (KG)} -$
24754.8	$\text{FORCE AT FOOT (NEWTONS) PER LEG WITHOUT PAD'S}$
9.8	$G = \text{FORCE OF GRAVITY (9.8 m/s}^2\text{)}$
0.030176	Corner Base Pad 0.184 X 0.164 Metre
820347	Pressure under Base Pad in N/m²
	DIVIDE F_1 BY AREA OF FOOT/PAD TO GIVE FORCE IN N/m²
820	kN/m² This is the pressure under one of the corners (the end pair being equally loaded) at the Generator and Battery end of the EcoLogic SOLAR Unit, which is therefore the maximum load on any one of the 4 Base Pads on which the Unit stands. NB. Use of Jack Leg would result in higher loadings because of area applicable. Pads NOT INCLUDED

Dav - Feb 2022

2. Details of Vehicle/Crane

Make & Model:	Rigid Scania 8 x 2 with minimum 80 Te Metre Class Fassi F820RA 2.28 Lorry Loader Crane.
Capacity:	72.17 Te/Metre
Outrigger Spread Centres:	Left to Right (X) Max 8.2 Metre Front to Back (Y) 7.3 Metres
Force through Outrigger Piston.	149862 Newton's – Refer to Page 5
Standard Mat/Pad Size:	800 mm Diameter Nylon Mats = 0.502 Sq M
Additional Outrigger Mat's available at additional cost:	Please refer to the quotation provided - 1.5 M x 1.2 M available.
Final maximum distributed Outrigger Load with standard Mat:	30.43 Te M Sq – Refer to Page 5
Gross Rigged Weight:	Max 40,000 Kgs

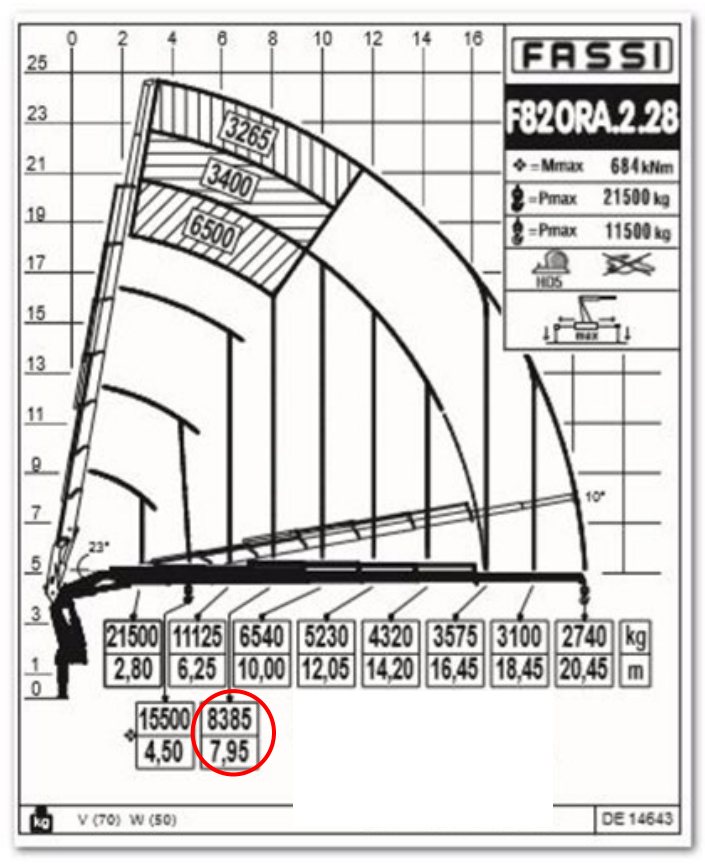




Lorry Loader Cross Section

Required operating clearance for Lorry Loader

11.65m (F)

Note 1

If larger pads are requested, add 250mm to required clearance for vehicle to allow for Pad Carrier. Therefore "B" will become 4.60m loaded height with Pad carrier

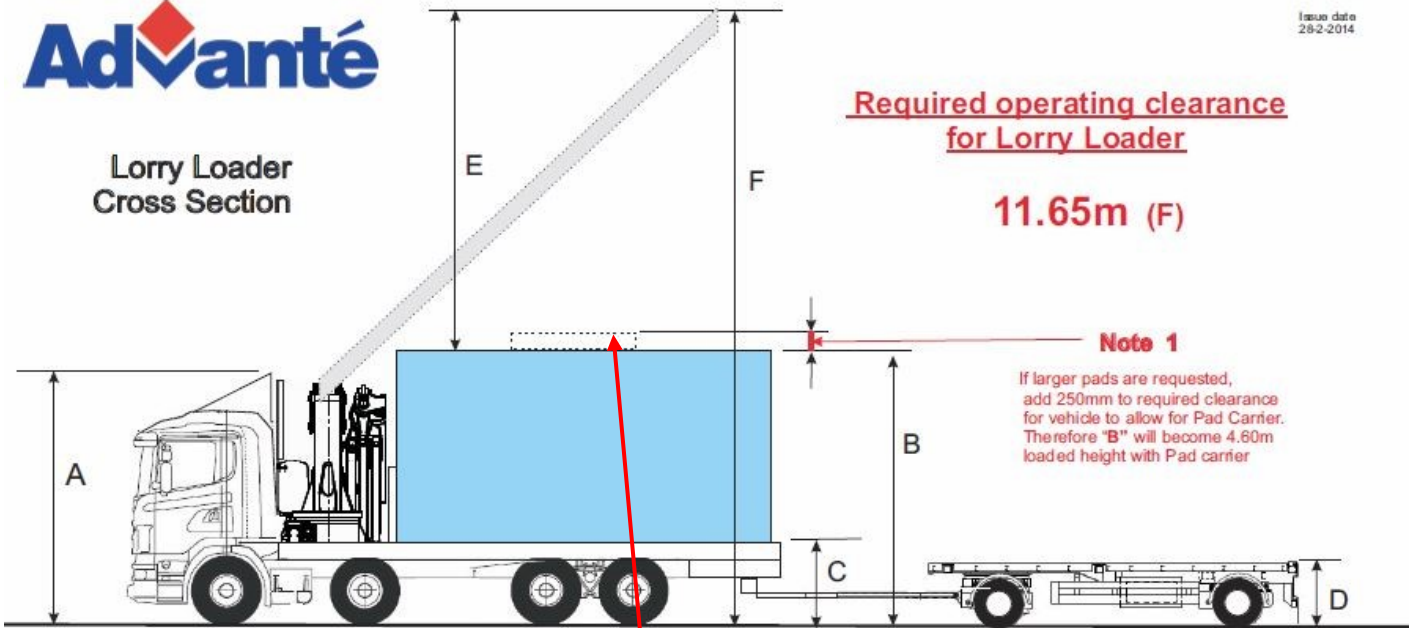

Lorry Loader height above Load					H
Unit Length (m) (2.7m wide)	Crane structure Top to Hook (m)	Master link (m)	Height to master link from unit roof (m)	Movement allowance (m)	Minimum height required above unit (m)
4.8	1.5	0.4	2.4	0.5	4.8
6.3	1.5	0.4	3.2	0.5	5.6
7.3	1.5	0.4	3.7	0.5	6.1
9.8	1.5	0.4	4.9	0.5	7.3

Lorry dimensions

- A 4.10m unloaded running height
- B 4.35m loaded height to top of unit
- C 1.25m lorry deck
- D 1.10m trailer deck

Note on B This is height for our highest unit (3.1m) other models are lower 2.65m) so dimension **A** then becomes the critical access measurement. (See Note 1 in red)
Note on F Clearance required varies according to unit size. See Table column **H** for specific dimension and add dimension **B** to **H** to obtain model specific value of **F**.


Larger Mats below available at additional cost as confirmed on the quotation provided.



3. Ground Conditions

Access/Egress:	Otherwise, suitable for vehicle configuration detailed, uninterrupted, hazard free to low-risk area UNDER escort from a Client Site Operative/Banksman. NB. The Lorry Loader Crane Operator has the right to raise any issues on arrival
Lifting Position:	Client to prepare the ground if required/accept the vehicle weight and distributed outrigger load for the standard Outrigger Mats confirmed. Suitable for uninterrupted, hazard free to low-risk area.

PRESSURE UNDER OUTRIGGER FOOT/PAD CALCULATION

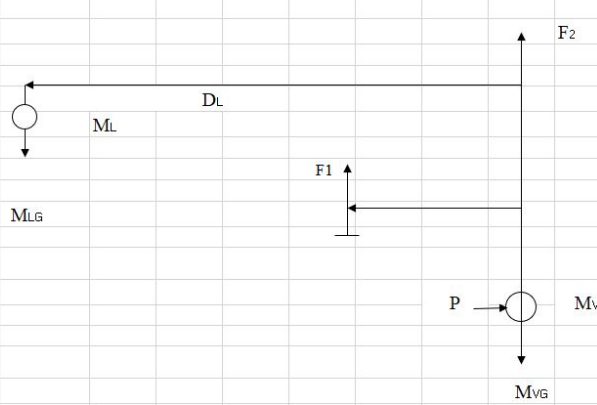

M_L = MASS OF LOAD (KG) –
 M_v = MASS OF VEHICLE (KG)
 D_f = DISTANCE FROM C/L OF COLUMN C/L OF FOOT (METRES) –
 D_L = DISTANCE FROM C/L OF COLUMN TO C/L OF LOAD (METRES) –
 (this is the maximum distance D_L will be.)
 F_1 = FORCE AT FOOT (NEWTONS)
 F_2 = FORCE AT VEHICLE (NEWTONS)
 G = FORCE OF GRAVITY (9.8 m/s^2)
 FORMULA FOR FORCE AT C/L OF FOOT, AS PARTICLE FORCE IS AS FOLLOWS:
 $F_1 = M_L G D_L$
 D_f
 DIVIDE F_1 BY AREA OF FOOT/PAD TO GIVE FORCE IN N/m^2

19-11-2010 ver3

Calculations for lifting a 32 Ft x 9 Ft EcoLogic or EcoMax SOLAR Welfare Unit with Advante Ltd Transport ONLY

Don't forget the king post on most cranes is offset so for maximum Outrigger extension the longest measurement is from the centre of the vehicle to the centre of the outrigger lift ram plus the offset. If you enter the loaders maximum lift at maximum extension this will give you the maximum pressure on an outrigger pad for any weight /radius combination possible on that vehicle

Data Table input	Enter information in yellow squares
7.95	Radius of lift from crane centre (DL) in Metres (example 3.45)
7500	Total weight of lift including chains or other lifting equipment (ML) in Kgs
3.9	Out rigger extension (DL) in metres, plus distance to centre of king post in Metres
Pad size	Pad's under out riggers 1000 by 502 mm
Standard Nylon Mat supplied with Crane = 0.8 Metre Diameter Nylon Disc = 0.5026 Sq Metres	


Don't forget if you want to calculate the load on the pad at less than the maximum Lorry Loader Crane lift at a radius, the total weight of a lift equals Load plus lifting equipment


Pressure under outrigger in N/m^2	
7500	M_L = MASS OF TOTAL LOAD (KG) –
24300	M_v = MASS OF VEHICLE (KG)
3.9	D_f = DISTANCE FROM C/L OF COLUMN C/L OF FOOT (METRES) –
7.95	D_L = DISTANCE FROM C/L OF COLUMN TO C/L OF LOAD (METRES) – (this is the maximum distance D_L will be.)
149826.92	F_1 = FORCE AT FOOT (NEWTONS)
9.8	F_2 = FORCE AT VEHICLE (NEWTONS)
0.502	G = FORCE OF GRAVITY (9.8 m/s^2)
	Foot pad 1 X 0.502 metre
298460	Pressure under outrigger in N/m^2
	DIVIDE F_1 BY AREA OF FOOT/PAD TO GIVE FORCE IN N/m^2
298	kN/m² 30.43 Tonnes /per M²
	This is the pressure under the Outrigger Pad with shortest distance from the Crane centre when fully extended at the total weight confirmed, therefore the maximum pressure on any one Outrigger

4. Lifting Accessories


Slings (Rope): N/A	Slings (Webbing): N/A
Slings (Chain): 1 No Set of 4 Leg 7 Metre Chain Brothers minimum combined SWL 8.4 Te per set fitted with Safety Hook's suitable to lift the EcoMax Unit's	Shackles: N/A
Other Accessories Used: N/A	

Lower lifting positions on the 32 Ft SOLAR EcoLogic Unit – Refer to Section 1 Page 2 product details

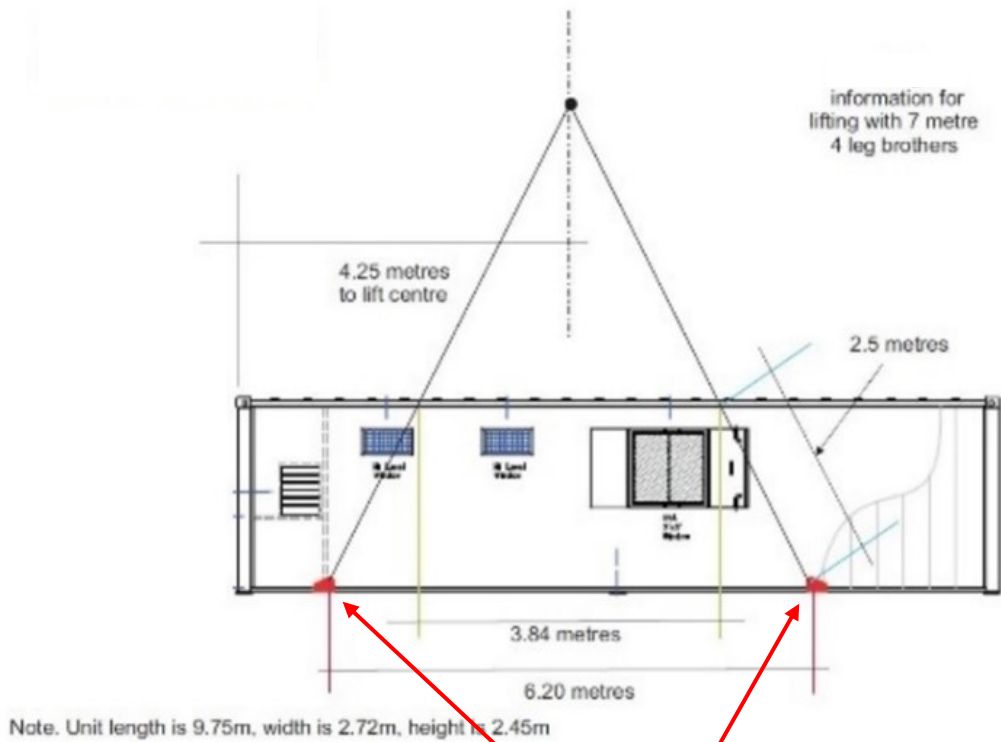

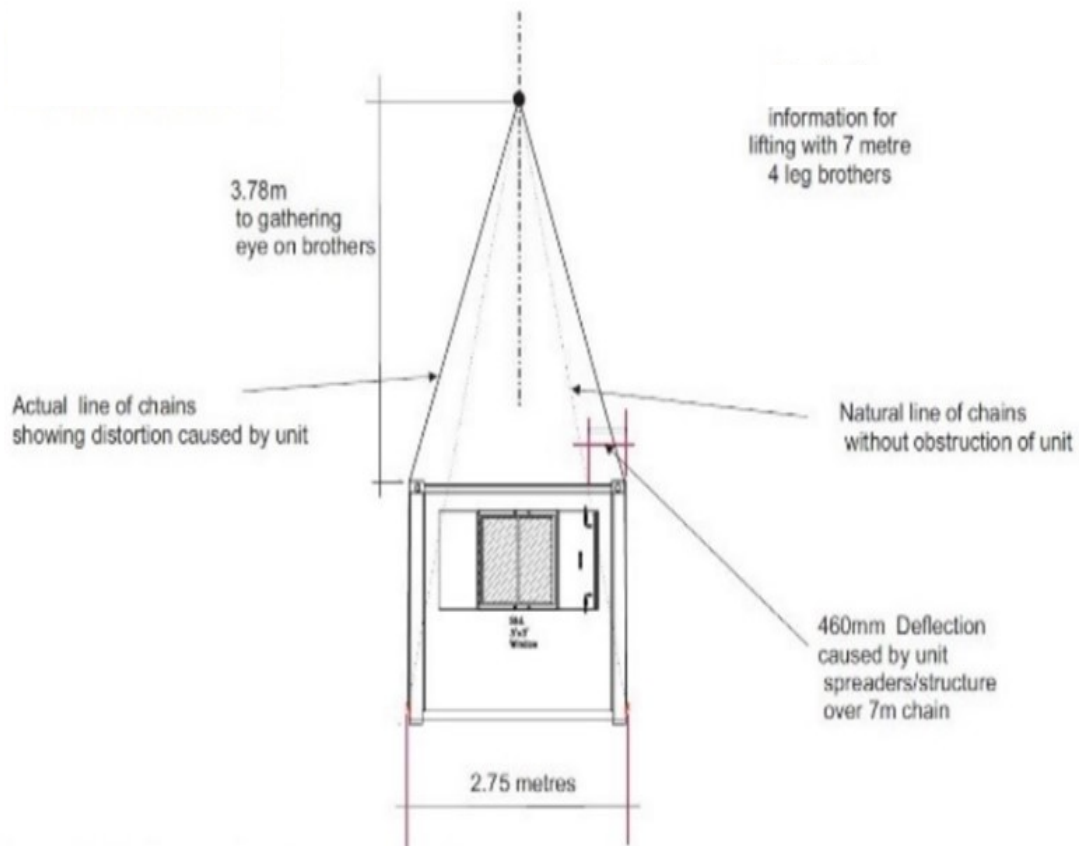

Top Lifting Positions (All SOLAR EcoMax Welfare Units)

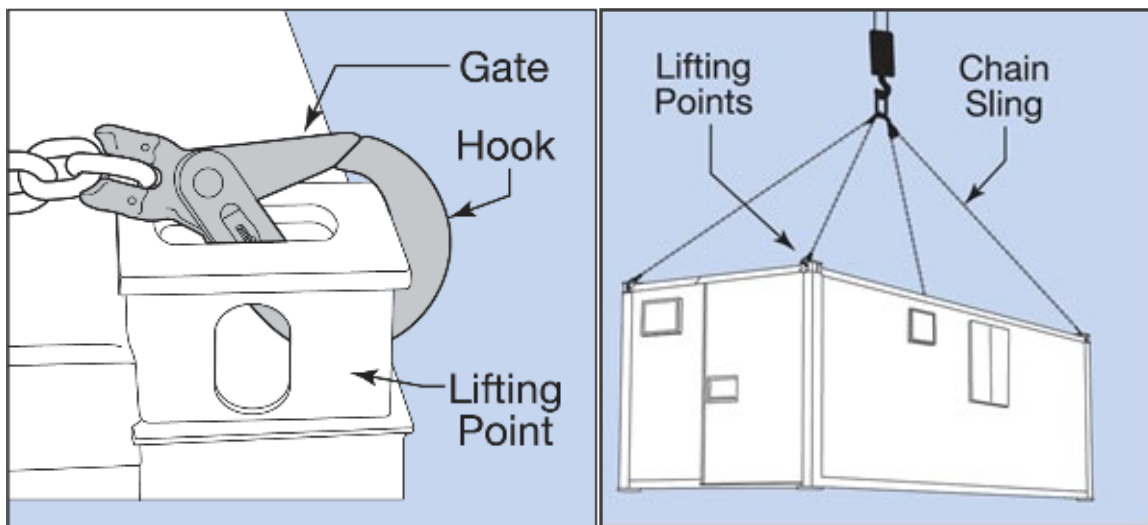

5. Hazards to be considered and assessed by Clients Site Management and confirmed prior to delivery.

Proximity Hazards	Present?	Proximity Hazards	Present?
Overhead Power Lines		Hazardous Chemicals/Materials	
Other Overhead Obstacles		Confined working Area	
Underground Services		Restricted Access - Width	
Excavations		Restricted Access - Height	
Unstable/Soft Ground		Other Vehicles	
Slinging Difficulties		Adjacent to Railway Line	
Other Hazards Identified			

6. Operational Requirements

Fall Arrest System with Auto-Descender in place for Working at Height procedures

Lorry Loader Crane Operator will operate the Lorry Loader Crane via a Waist positioned Remote Control Console working to client management approval and with client nominated operatives.

If necessary, the Lorry Loader Crane Operator can operate alone using Remote Control Console under strict control procedures to be assessed and informed to the Client. Refer to Risk Assessment Section 13

7. Customer Provisions

Client to organise and maintain all traffic control, demarcation of the working area, control of the Lorry Loader Crane and other traffic for access/egress, preparation of suitable area to receive the EcoLogic Unit(s), freely available induction if required and all welfare/operation support of Advanté staff while on site

8. Personnel:

Title	Responsibility	Required PPE
Crane Supervisor – To be provided by Client/Site Manager	Oversee all below	Hi-Vis Waist Coats or Jackets BSEN471 Toe Protection Safety Boots BSEN 346 Gloves BS1651 Safety Glasses/Goggles DIN EN166 Hard Hat BSEN 397
Slinger/Signaller Combined Role with Crane Operator	Attach/detach Lifting Chains to and from the Welfare Unit, signal the movement of the crane and load on the Crane Hook with assistance from client nominated site operatives restraining the Tag Lines	Hi-Vis BSEN471 or Jackets BSEN471 Harness – Advante Operatives use a Cradle Harness BSEN 361:2002. External Re-Hired Operatives may use alternative specifications to minimum BSEN 361 Inertia Reel BS EN 360:2002 Toe Protection Safety Boots BSEN 346 Gloves BS1651 Safety Glasses/Goggles DIN EN166 Hard Hat BSEN 397
Lorry Loader Crane Operator	Correct operation of the Lorry Loader Crane in accordance with the manufacturer’s instructions.	Hi-Vis BSEN471 or Jackets BSEN471 Toe Protection Safety Boots BSEN 346 Gloves BS1651 Hard Hat BSEN 397 Safety Glasses/Goggles DIN EN166

9. Lifting Accessories

The lifting accessories will be provided by Advanté Ltd and supported by valid Certificates of Thorough Examination.

10. Weather Conditions

The lifting operation can only take place if the weather conditions are within the limits recommended by the crane manufacturer of a maximum 13.9 M/S less an allowance for the surface area of the Welfare Unit to be lifted.

Wind speeds measured by handheld Anemometer – These devices are used for indication purposes only.

11. Ground Conditions

It is the Client's responsibility to check before the lift is undertaken to determine that the ground is suitable and as such Advanté Ltd. will not be responsible for any liabilities and / or damage to surfaces that arise from the ground conditions not being suitable to allow access / egress and lifting operations to be carried out.

12. Trading Conditions

CPA., FTA.

13. Lifting Conditions

CPA Supplementary Conditions Applicable to Mobile Cranes (Wheeled & Crawler Mounted) 2011

Sequence of Works

Note	<i>The Advanté Delivery & Collection RAMS supporting these works accompanies this Method Statement and will be valid at the point of undertaking site activities – this document is subject to regular changes and the current version will always be provided at the point of service delivery.</i>
1	Arrive at site and the Lorry Loader Crane Operator (LLCO) will report to the Client Site Management (C SM) at the pre-arranged time above for traffic guidance and receive any updates to previously advised controls relevant to current site conditions.
2	The LLCO will make available all Crane, Lifting Tackle, Harness and personnel/training documentation to the C SM and with the assistance from the C SM, this will be entered the Site/Safety Inspection Register to prior to any work commencing.
3	The LLCO will liaise with the C SM and nominated Client Site Operatives (C Ops) in respect of demarking and controlling the safe working area for the operation of the Lorry Loader Crane (LLC) and the unloading activities corresponding with the maximum unloading radius confirmed in Section 1 Page 2. Note in the absence of input from the C SM/C Ops, the LLCO's will define the safe working area and Mark Out using Hatched Tape and display Hazard Warning Beacons/Lights on the LLC throughout the operation.
4	With C SM approval to proceed and displaying Hazard Warning Beacons, the LLC will now enter the site under guidance from C Ops to the unloading position required to correspond with the unloading detail confirmed in the accompanying Drawing.
5	The LLCO and C SM will verify that no additional hazards are present within the lifting position at both ground level and overhead and that all conditions have been met as set out in the Risk Assessment & Method Statement.
6	The LLCO to then attend (if required) the Site Induction and C SM will issue the Permit to Lift and if required, a Permit for the Use of Ladders. Included in the Induction will be the location of the nearest A & E Hospital and Non-Emergency Medical Centre and this will be included in the Action Plan to be confirmed by the C SM.
7	With C SM approval to proceed, the LLCO will then recheck that the isolated area remains clear and from an operating position on each side of the LLC, extend the Crane Stabiliser Beams to the maximum width, recheck for the position of any Utility Covers/changes in the surface to be set up on and position the standard Outrigger Mats carried on the LLC.
8	The LLCO will then extend the Outrigger Rams to stabilise the Crane ensuring the Wheels are in contact with the ground, the suspension is not completely unloaded and carry out any pre-operational checks in accordance with the manufacturer's recommendations. NB. If the additional Outrigger Mats are requested and confirmed on the official order to be received, these are delivered on the Pad Carrier (Refer to Page 5 Diagram of the Lorry) located on the roof of the Welfare Unit and will be unloaded/positioned corresponding with Items 6 and 11 of the Risk Assessment Document.
9	The LLCO will check the weather conditions comply with the lifts to be carried out and select the Lifting Chain Leg Brothers required to lift the 32 Ft SOLAR EcoLogic Unit (EL Unit) and then control the Crane and carry out the motions required to position the Boom with the Lifting Chains at the rear of the EL Unit.
	Continued next Page

10	The LLCO will then “Pair Up” the Lifting Chains for each side of the EL Unit and Tag Lines will be attached. Working with C Ops, the LLCO will then restrain the Tag Lines to separate the Pairs of Lifting Chains and keep the Lifting Chains clear of the roof mounted PV Panels.
11	The LLCO will then control the Crane and carry out the motions required to position the Boom and slowly guide the separated Lifting Chains down the sides of the EL Unit for attachment to all four lower position lifting points. Refer to the detail on Pages 2 and 7
12	NOTE FOR TOP LIFTING POSITIONS ONLY IF REQUIRED – The Lifting Chains will then be attached to all four corner lifting points via the use_of a Pre-inspected Ladder fitted with a ground level Stabiliser Bar (as per the RA) and using a Harness and Fall Arrest as per the RA. The Ladder MUST be positioned on suitable level ground and if necessary footed by C Ops.
13	Tag Line’s will then be attached to each end of the EL Unit to enable C Ops to control the EL Unit. The LLCO will carry out a visual check of the Lifting Chains/lifting positions, the position of the Crane Hook and check that all involved are ready and will be in a Visual or Audible position at all times throughout lifting the EL Unit.
14	With the C SM approval to continue, the LLCO will control the Crane to carry out the motions required to lift the EL Unit just clear from the transport position and STOP. The LLCO will check that the EL Unit has lifted in a level position and the Lifting Chains remain secure.
15	When the checks are completed and with the EL Unit being restrained by the Tag Lines, the LLCO will control the Crane and carry out the motions required to slew to the installation position required.
16	Prior to the EL Unit being lowered, a visual check of any hazards must be conducted including the positions of all personnel involved in the lifting operation and continued consideration given to any other activities on the perimeter of the isolated area.
17	Once clear/checks are completed, the EL Unit can now be lowered into position and levelled using any C SM provided “Packing” that is required/the adjustable feet of the EL Unit.
18	The LLCO will now control the Crane to take the tension off the Lifting Chains that will then be detached from the Four lower lifting positions. The LLCO will then “Pair Up” the Lifting Chains on each side of the EL Unit and Tag Lines attached to be restrained by C Ops
19	The LLCO will then control the Crane to carry out the motions required to slowly position the Lifting Chains clear of the EL Unit to prevent the Lifting Chains from Snagging on the side of the EL Unit and coming in to contact with the roof mounted PV Panels.
20	NOTE FOR TOP LIFTING POSITIONS ONLY IF REQUIRED – Repeat Operations 12 and 19 relevant to detaching the Lifting Chains and to avoid damaging the PV Panels.
21	On completion of the lifting operations, the LLCO will then stow away the lifting tackle and complete the derig procedures of the Crane as per the manufacturers recommended instructions.
22	The LLCO will carry out checks in preparation to leave site and under guidance from C Ops, the individual LLC’s will be escorted back to the site entrance and out of the Public Road system to leave safely in the direction required. For collection of the EL Unit, repeat Operations 1 to 22 in a sequence relevant to removing the EL Unit from site.



Hired & Managed Advisory General Method Statement – Advanté Welfare
